



COUNTY OF WELLINGTON

COMMITTEE REPORT

To: Chair and Members of the Roads Committee
From: Joe de Koning, Manager of Roads
Date: Tuesday, September 13, 2022
Subject: **2022 Road Capital Construction – Project Status**

Background:

This report provides the committee with information on the status of 2022 road capital construction projects. The following summary is based on the project status as of August 31, 2022:

Current Construction

- **CW2021-021 WR 45 Slope Stabilization**, (Mapleton) – Kieswetter Excavating – Work will be completed by October
- **CW2022-008 WR 16 Rehabilitation of Penfold Bridge (B016038)**, (Centre Wellington) – Engineered Concrete – Work will be completed by mid September
- **CW2022-015 Pavement Overlay**, (various locations) – Cox Construction – Work was completed in June
- **CW2022-016 WR 7 Rehabilitation Marden Creek Bridge (B007071) and Asphalt Rehabilitation**, (Guelph-Eramosa) – Cox Construction – Work completed in August
- **CW2022-017 WR 22 at 2nd Line to Hilltop Blvd**, (Town of Erin) – Cox Construction – Work to be completed by late October
- **CW2022-018 WR 38 Asphalt Rehabilitation**, (Guelph-Eramosa) – Cox Construction – Work completed in August
- **CW2022-019 WR 12 Culvert (C120127) Replacement**, (Mapleton) – Cox Construction – Work completed in June
- **CW2022-043 WR 50 Surface Asphalt**, (Town of Erin) – Cox Construction – Work completed in June

Future Construction

- **CW2022-020 WR 7 Bosworth Bridge (B007028)**, (Mapleton) – Anticipate tender in December 2022
- **CW2022-021 WR 17 Creekbank Bridge (B017040)**, (Centre Wellington)- Anticipate tender in December 2022

Shared Construction Projects

- **WR 5 Lett St, Minto**, Shared project with Town of Minto – Work to be completed in October
- **WR 86 – Wallenstein**, (Mapleton) - Shared project with Region of Waterloo – Work to be completed in October

Miscellaneous

- **CW2022-041 WR 34 Irish Creek Bridge (B034123)**, (Puslinch) – Project was not awarded and work to be postponed until 2024

2022 Summary

• Construction Costs (approximate)	\$ 14,500,000.00
• Major Culvert Replacements	1
• Bridge Rehabilitations or Replacements	1
• Road Preservation (Overlays)	11.5 km
• Road Renewal	15 km

In addition to the 2022 construction project work, carryover projects were also completed during the current construction season:

- **T2021-153 WR17 ROW to Floradale Road Paving/Recycling**, (Mapleton) - Cox Construction. Recycling and paving of 1.5 km of road shared with the Region of Waterloo. Work also includes a bridge rehabilitation. Construction was completed in June 2022.

Recommendation:

That the report titled “2022 Road Capital Construction – Project Status” be received for information.

Respectfully submitted,

A handwritten signature in black ink, appearing to read 'Joe de Koning', with a large, stylized initial 'J' and 'K'.

Joe de Koning, P. Eng.
Manager of Roads



Attachment: Construction 2022 Project Map



WELLINGTON COUNTY

2022 Road Capital Construction Project Status

- BRIDGE & CULVERT CAPITAL CONSTRUCTION
- CW2022-015 PAVEMENT OVERLAY
- INTERSECTION IMPROVEMENTS
- 2022 ROAD CAPITAL CONSTRUCTION
- URBAN CENTRE
- WATERBODY
- MUNICIPAL BOUNDARY

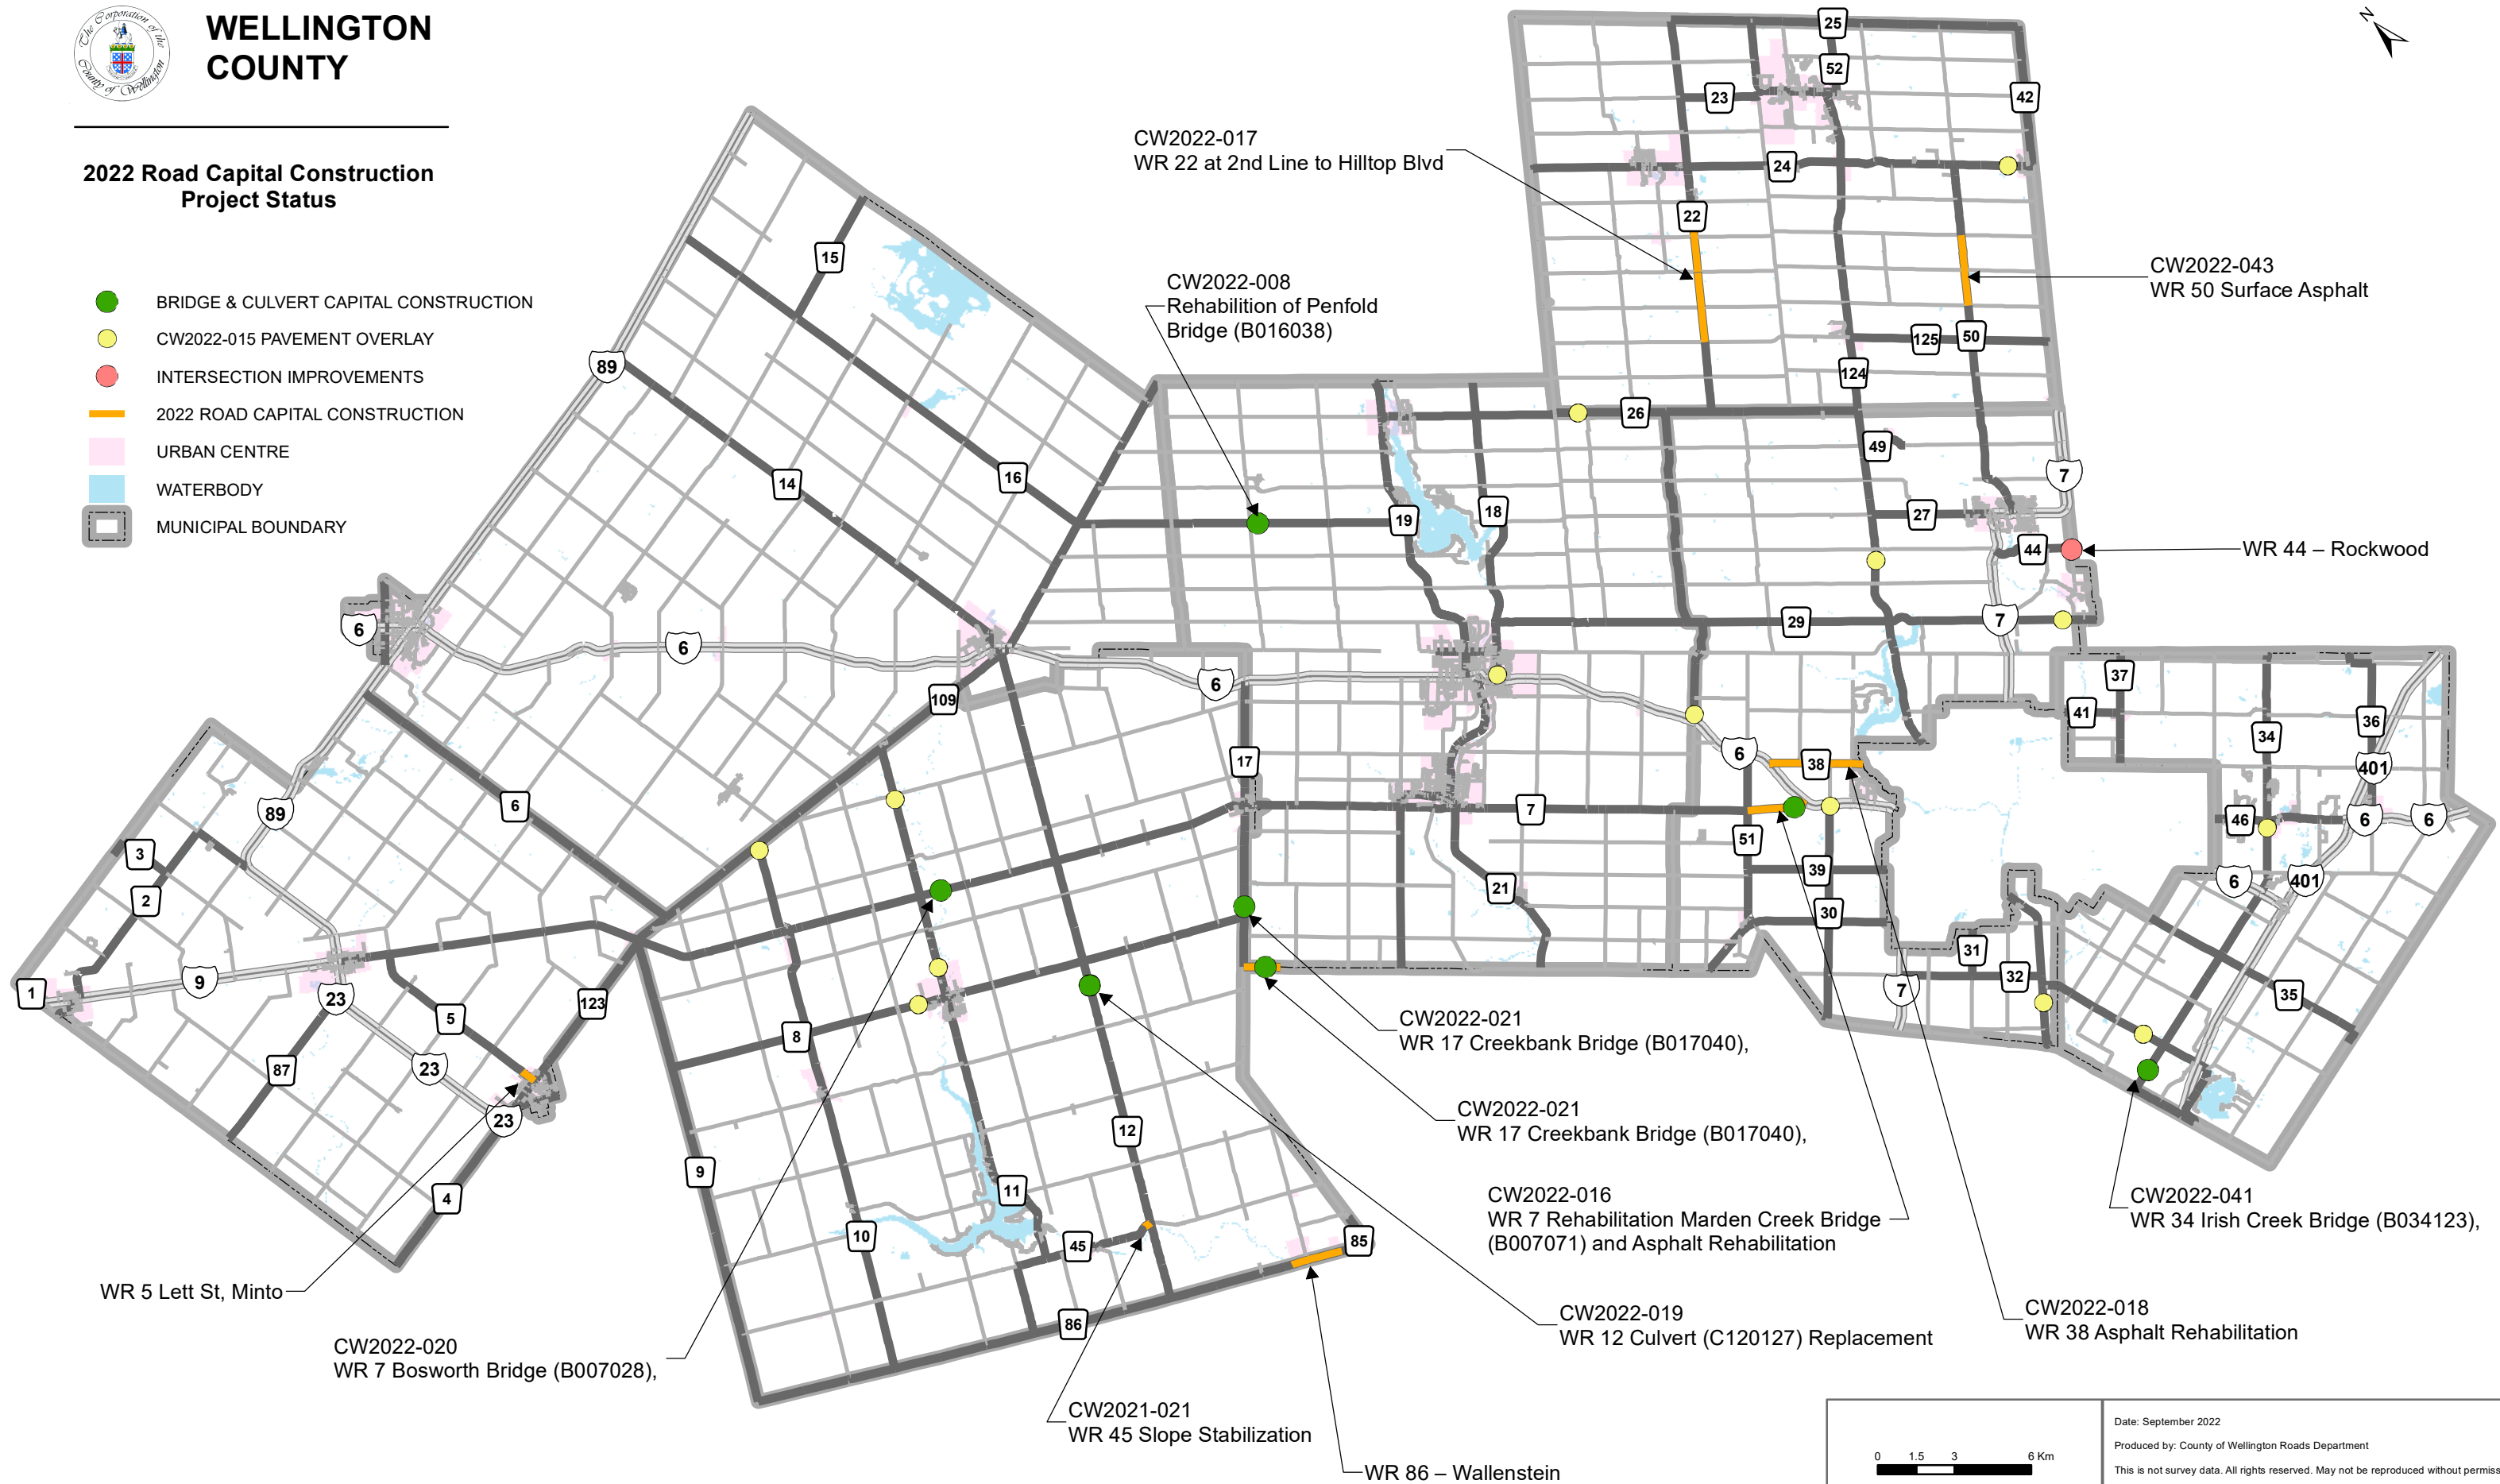

Date: September 2022
Produced by: County of Wellington Roads Department
This is not survey data. All rights reserved. May not be reproduced without permission.
Sources: County of Wellington, MNR, GRCA
INCLUDES MATERIAL ©2015 OF THE QUEEN'S PRINTER FOR ONTARIO. ALL RIGHTS RESERVED
2020 Ortho imagery.
